

Waskada Unit No. 13

Waterflood Progress Report 2019

January 1st through December 31st 2019

Prepared for:

Manitoba Industry, Economic Development and Mines

Petroleum Branch

Prepared by:

Tundra Oil and Gas


March 18, 2020

INTRODUCTION

Waskada Unit No. 13 Enhanced Oil Recovery (EOR) Waterflood Project was approved under Board Order No. PM 58 effective December 1986. The Unit area contains 13 abandoned/suspended wells, including 5 abandoned/inactive injectors, and 15 producing/inactive wells in 15 LSDs in Township 2, Range 26 W1 as shown in the figure below.

This unit is currently not on injection and there are no plans for injector re-activation .

Figure 1: Waskada Unit No. 13 Area Outline

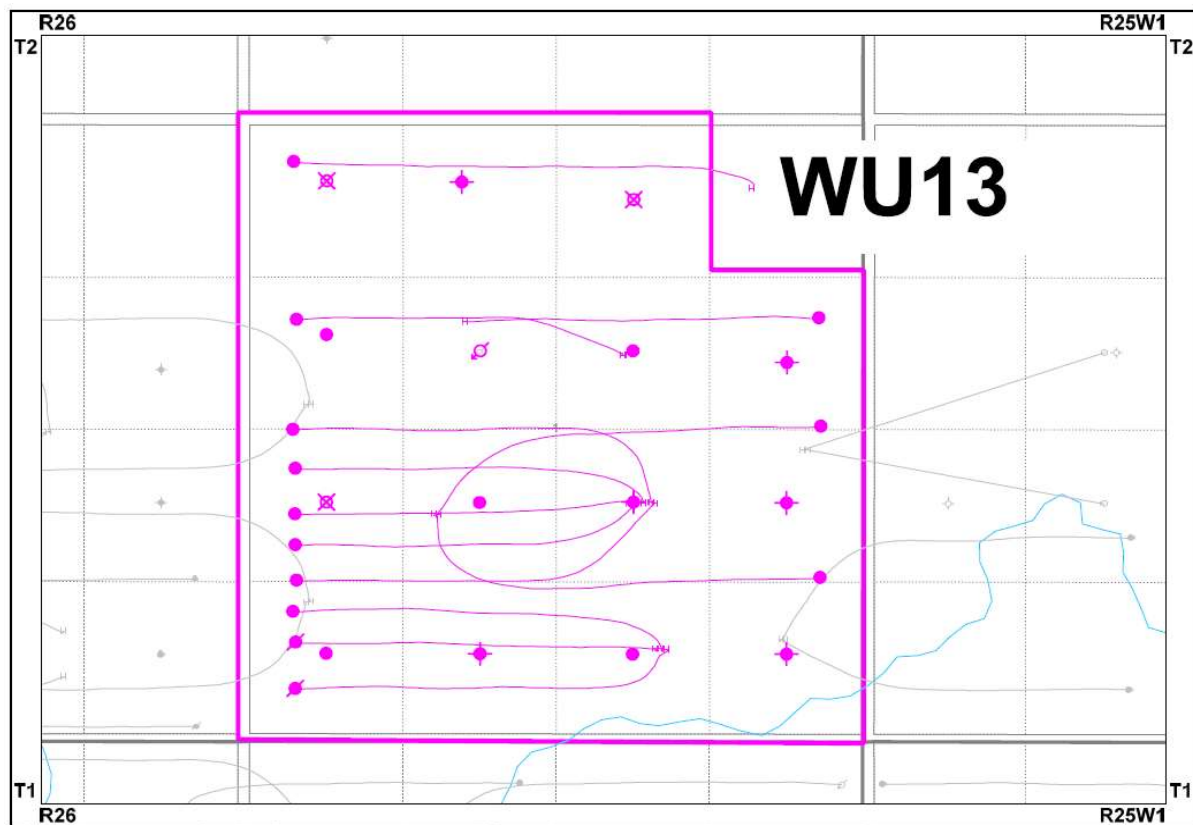

Waskada Unit No. 13

Tundra Oil and Gas (Tundra), as the operator of the Waskada Unit No. 13 Enhanced Oil Recovery (EOR) project hereby submits the 2019 EOR report as per section 73 of the Drilling and Production Regulations.


a) Monthly oil and water production rates, injection rate, GOR and WOR

MONTH	Cal Dly Oil m ³ /day	Cal Dly Wtr m ³ /day	Cal Inj Wtr m ³ /day	WOR m ³ /m ³	GOR m ³ /m ³
Jan-2019	0.91	1.00	0.00	1.10	0
Feb-2019	0.01	0.01	0.00	1.50	0
Mar-2019	0.08	0.09	0.00	1.17	0
Apr-2019	1.28	1.41	0.00	1.10	0
May-2019	1.19	1.02	0.00	0.86	0
Jun-2019	0.90	0.71	0.00	0.79	0
Jul-2019	0.93	0.54	0.00	0.58	0
Aug-2019	0.75	0.56	0.00	0.75	0
Sep-2019	0.56	0.39	0.00	0.69	0
Oct-2019	0.70	0.48	0.00	0.68	0
Nov-2019	0.62	0.29	0.00	0.47	0
Dec-2019	0.18	0.12	0.00	0.63	0

b) Cumulative volume of oil, gas and water produced and fluid injected

2019 PRODUCTION	
Produced Oil (m ³)	248
Produced Gas (m ³)	0
Produced Water (m ³)	202
Fluid Injected (m ³)	0
CUMULATIVE PRODUCTION	
Produced Oil (m ³)	105,472
Produced Water (m ³)	81,383

Waskada Unit No. 13

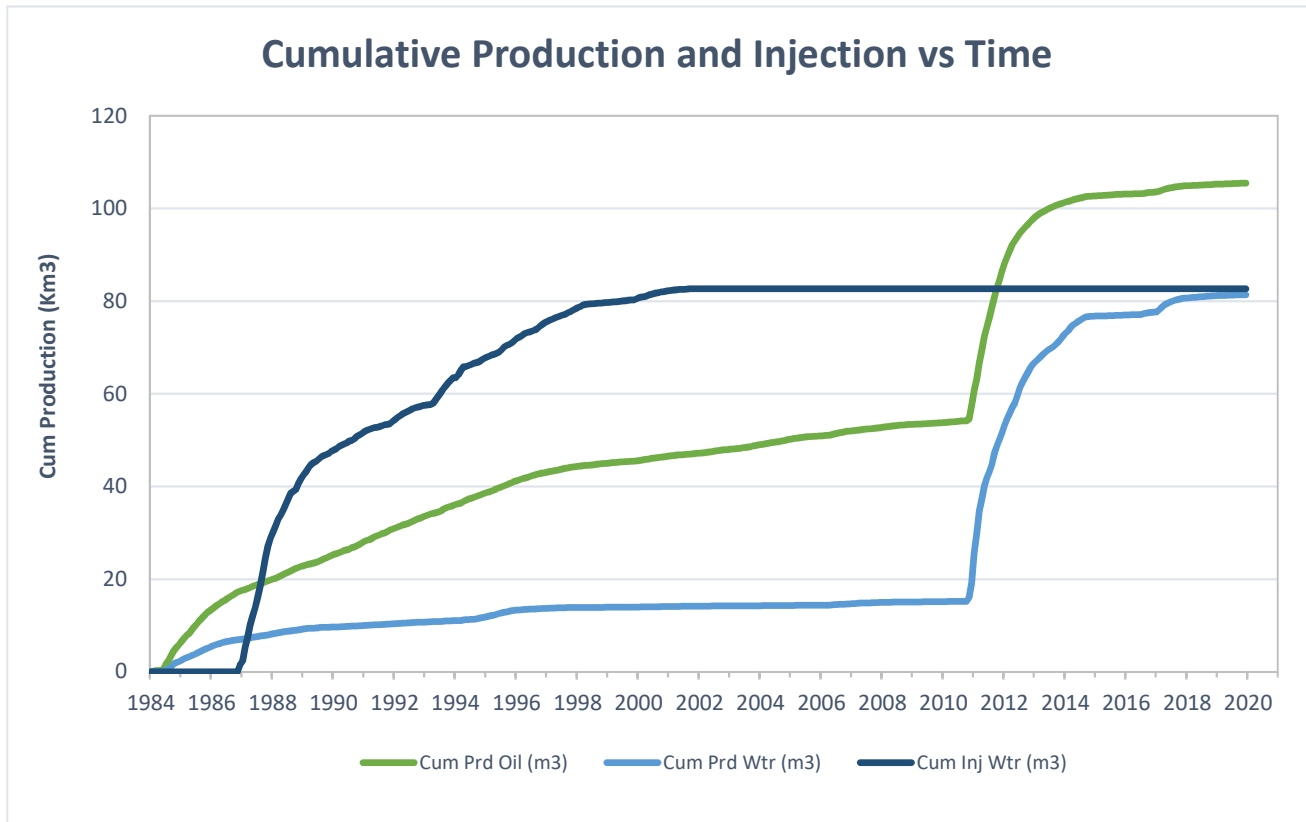

c) Well List

Waskada Unit No. 13 Well List

<i>UWI</i>	<i>Type</i>	<i>Status</i>	<i>Future Plans</i>
100/01-01-002-26W1/0	Vertical	Abandoned	-
100/02-01-002-26W1/0	Vertical	Producing	-
100/03-01-002-26W1/0	Vertical	Abandoned Zone	-
100/04-01-002-26W1/0	Vertical	Producing	-
102/04-01-002-26W1/0	Horizontal	Producing	-
103/04-01-002-26W1/0	Horizontal	Suspended	-
104/04-01-002-26W1/0	Horizontal	Producing	-
105/04-01-002-26W1/0	Horizontal	Suspended	-
100/05-01-002-26W1/0	Vertical	Abandoned	-
102/05-01-002-26W1/0	Horizontal	Producing	-
103/05-01-002-26W1/0	Horizontal	Producing	-
104/05-01-002-26W1/0	Horizontal	Producing	-
105/05-01-002-26W1/0	Horizontal	Producing	-
100/06-01-002-26W1/0	Vertical	Producing	-
100/07-01-002-26W1/0	Vertical	Abandoned	-
100/08-01-002-26W1/0	Vertical	Abandoned	-
102/08-01-002-26W1/0	Horizontal	Producing	-
100/09-01-002-26W1/0	Vertical	Abandoned	-
102/09-01-002-26W1/0	Horizontal	Producing	-
103/09-01-002-26W1/0	Horizontal	Suspended	-
100/10-01-002-26W1/0	Vertical	Producing	-
100/11-01-002-26W1/0	Vertical	Injection	-
100/12-01-002-26W1/0	Vertical	Producing	-
102/12-01-002-26W1/0	Horizontal	Producing	-
100/13-01-002-26W1/0	Vertical	Abandoned	-
102/13-01-002-26W1/0	Horizontal	Producing	-
100/14-01-002-26W1/0	Vertical	Abandoned Zone	-
100/15-01-002-26W1/0	Vertical	Abandoned	-
